



NorthStar Group Services, Inc.

2760 South Falkenburg Road, Riverview, FL 33578

Phone: 203.222.0584 | Fax: 212.951.8975

www.NorthStar.com

Gregory G. DiCarlo

Vice President and General Counsel

gdicarlo@NorthStar.com

March 31, 2020

Commissioner Vermont Department of Public
Service 112 State Street-Drawer 20

Montpelier, VT 05620-2601

Sent via e-mail to June.Tierney@vermont.gov

Director for Public Advocacy

Vermont Department of Public

Service 112 State Street - Drawer 20

Montpelier, VT 05620

Sent via e-mail to Eric.Guzman@vermont.gov

Sent via e-mail to James.Porter@vermont.gov

Re: Report Pursuant to MOU Section 2(h)

Dear Commissioner Tierney:

Enclosed please find NorthStar Vermont Yankee, LLC's report submitted in accordance with Section 2(h) of the Memorandum of Understanding for Docket No. 8880 dated March 2, 2018 ("MOU"). Please note that NorthStar has copied the relevant MOU provisions and provides its response in underline.

Very truly yours,

Gregory G. DiCarlo

Vice President and General Counsel

Attachments

MOU Section 2(h)

On or before March 31 of each calendar year following the close of the Proposed Transaction, NorthStar shall provide to DPS, ANR, VDH, and AGO an annual public certification that includes the following:

(1) A detailed description of all work completed as of that date pursuant to corrective action plans approved by ANR pursuant to Subchapter 5 of the IRule.

Answer: There are no corrective action plans approved by ANR to date, with anticipation of corrective action plans in 2020 as noted below from works conducted in 2019.

(2) A detailed description and schedule of remaining corrective actions and site restoration work.

As noted on the 2018 Annual Report for Site Restoration and Characterization work following the formal sale closing, NorthStar formally submitted the following documents to ANR electronically;

1. Limited Non-Radiological Site Sampling Plan, Rev F
2. Appendix A: Below-Grade Structure Survey Work Plan
3. Appendix B: Borrow Materials Import Plan
4. Appendix C: Groundwater Monitoring Plan
5. Appendix D: Concrete Reuse Plan
6. Quality Assurance Project Plan, Rev E

Following a February 28, 2019 meeting between VT ANR and its contractor, ATC, to review the details of the restoration and characterization plans prepared in 2018, and a follow-on site tour conducted on March 15, 2019, VT ANR provided comments and approved concurrent activities for NorthStar to finalize the plans and also execute the field activities in anticipation of comments and requirements in order to get to a Final Site report that would result in closure of Areas of Concern or Corrective Actions as necessary.

Below are the work tasks and noted documents that were completed that resulted on the submission of the noted documents above being able to be submitted to VT ANR:

- Updated Draft Characterization Phase 1 Report
- Voluntary Removal Plan, Rev 0
- Voluntary Removal Plan, Rev 1
- Legal Support/Permit Support
- Building Material Characterization WP, Rev 0
- Building Material Characterization WP, Rev 1
- Building Material Characterization WP, Rev 2
- Final Draft Characterization Phase 1 Report

- Phase 2 Sampling Plan Data Quality Objectives (DQOs)
- Phase 2 Sampling Plan Rough Draft
- Phase 2 Sampling Plan First Draft
- Phase 2 Waste Area Group (WAG) Identification Plan Outline
- Phase 2 WAG Identification Plan Rough Draft
- Phase 2 WAG Identification Plan First Draft
- Phase 2 Update of Voluntary Removal Plan (D2) - Initial
- Phase 2 Update of Voluntary Removal Plan (D2) -Final
- Phase 3 Draft Remedial Action Scope and Schedule
- Phase 3 Provide Rough Draft RAWP
- Phase 3 Interim Draft RAWP - D1
- Phase 3 Final Draft RAWP - D2
- Phase 3 Review Data from Sampling for Waste Profiles
- Limited Characterization Sampling: Preparation
- Limited Characterization Sampling: Sampling Labor
- Limited Characterization Sampling: Analytical
- Limited Characterization Sampling: Data Report
- Site Investigation - Site Sampling WP, Rev D
- Site Investigation - Corrective Action Plans (drafts)

Upon receiving comments from VT ANR on the Work Plans, NorthStar conducted supplemental field Sampling to generate an updated Site Investigation Report that would depict non-Radiological conditions at the Vermont Yankee. These Site Investigation tasks included the following activities;

- Site Investigation – Vermont ANR Meetings
- Site Investigation Data Gap Report and Investigation
- Site Investigation - Site Investigation Schedule generation
- Site Investigation - Training
- Site Investigation - Site Investigation Field Sampling for Supplemental Data Gaps
- Site Investigation - SI Report with Validation, Rev 0 and 1
- Site Investigation - Non-Radiological Groundwater Sampling WP (1Q 2019), Rev A and B
- Site Investigation - Qtrly Non-Radiological Sampling & Reporting (2Q, 3Q, and 4Q 2019)
- Additional VT ANR Meetings (Restoration and Characterization)
- Additional Site Investigation Data Collection for the updated Site Investigation Report
- Vermont ANR and Subcontractor Coordination during Supplemental Data Field Sampling

- Additional Vermont ANR Meetings (Restoration and Characterization reporting)
- Updated Site Investigation Report (draft 4Q 2019)

The tasks and work items noted above supported generation of data that was incorporated into the final Updated Site Investigation Report that was submitted to Vermont ANR on January 31, 2020. Following this submission will be the resulting Corrective Action Plans for areas of concern that will be addressed in 2020. Following is a Table of Areas of Concerns:

Area of Concern	Investigation of Accessible Areas Complete?	Remediation Needed?	Remaining Data Gaps	Crosswalk to Decommissioning Work Breakdown Structure (WBS)
AOC 1 - 345 kV Switchyard	Yes	No	VELCO has a 99-year lease: soils within the yard will require characterization when lease expires.	
AOC 2 - 115 kV Switchyard	Yes	No	VELCO has a 99-year lease: soils within the yard will require characterization when lease expires.	
AOC 3 - South Warehouse	Yes	Yes	Limited shallow soil removal required, followed by confirmatory soil sampling	
AOC 4 - Former North Warehouse	Yes	No	N/A	
AOC 5 - Turbine Building	Yes	No	Soils under shallow foundations to be evaluated after removal.	1.04.11 Areas A6 - Chemistry Lab Drain Line 1.04.27 Area C100 - Turbine Building Clean Up Sump


Area of Concern	Investigation of Accessible Areas Complete?	Remediation Needed?	Remaining Data Gaps	Crosswalk to Decommissioning Work Breakdown Structure (WBS)
AOC 6 - Rad Waste Storage Building	Yes	No	Soils to be evaluated following slab removal	<p>1.04.06 Area A5 - Northeast Side of Radwaste Building</p> <p>1.04.17 Areas C86 & 87 - Sandblast Debris East of Radwaste Building</p>
AOC 7 - Fuel Storage Tanks	Yes	Yes	Former UST SW of Turbine Building; impacted soil along piping associated with the 75,000-gal FOST; and small stained area SW of the Shipping & Receiving Building. For each area, fuel oil/diesel impacted (PAH) media to be excavated & disposed off-site. Confirmatory sampling to follow.	
AOC 8 - Transformers	Yes	Yes	Area directly under ABB/Main transformer. To be coordinated with AOC 5 remediation of former UST location. A small area of shallow soil adjacent to the East Cooling Tower Transformer pad will	

Area of Concern	Investigation of Accessible Areas Complete?	Remediation Needed?	Remaining Data Gaps	Crosswalk to Decommissioning Work Breakdown Structure (WBS)
			also require removal and off-site disposal followed by confirmatory soil sampling.	
AOC 9 Intake and Discharge Systems	Yes	No	N/A	
AOC 10 - Parking Lots	Yes	No	To be evaluated after pavement is removed	
AOC 11 - Haz Materials Storage Areas	Yes	No	Soils to be evaluated following warehouse slab and Haz Stor shed removal.	
AOC 12 Former Edson's Gulf Station	Yes	Yes	Limited PAH-impacted soil excavation and confirmatory sampling	
AOC 13 - Septic Systems	Yes	Yes	Potential PFAS in leach fields and residual spreading area (South Application Field), as well as limited PAH impacted areas and stockpiles (North Application Field).	<p>1.04.10 Areas B1 - Septic System Sludge</p> <p>1.04.13 Areas B2 - Excavated Material Pile from PA Mods</p> <p>1.04.14 Areas B3 - Septic System Tanks</p> <p>1.04.15 Areas B5 - North 40 of Owner Controlled Area</p>
AOC 14 - Stormwater Outfalls	Yes	TBD	Risk assessment to evaluate sediments	1.04.03 Area A3 - North Storm Drain Outfall River

Area of Concern	Investigation of Accessible Areas Complete?	Remediation Needed?	Remaining Data Gaps	Crosswalk to Decommissioning Work Breakdown Structure (WBS)
				Bank 1.04.04 Area A4 - Manhole 12 Area A4 - South Strom 1.04.05 Drain System
AOC 15 - Cooling Tower Area	Yes	Yes	Soil piles to be used for shipping, or evaluated via risk assessment	1.04.07 Area B2 - Area Near West Cooling Tower 1.04.12 Areas B1 - Deep Basin Colling Tower Silt 1.04.16 Areas B6 - Burn Area
AOC 16 - Railroad Lines	Yes	Yes	Risk assessment required to further evaluate pesticide and PAH impacts to shallow soils, and potential limited soil removal	
AOC 17 - Sitewide Groundwater	Yes	No	Limited MNA, no active GW treatment needed	

An indication of the progress of Site Restoration and Characterization activities in relation to the Vermont ANR (I-Rule) for the chemical site closure process is depicted on the following figure:

MCELENEY, TERRI Printed: 2/4/2020 4:29 PM Layout: PRE02
 J:\GRAPHICS\129657\129657-009 PRE02 2019-1204.DWG

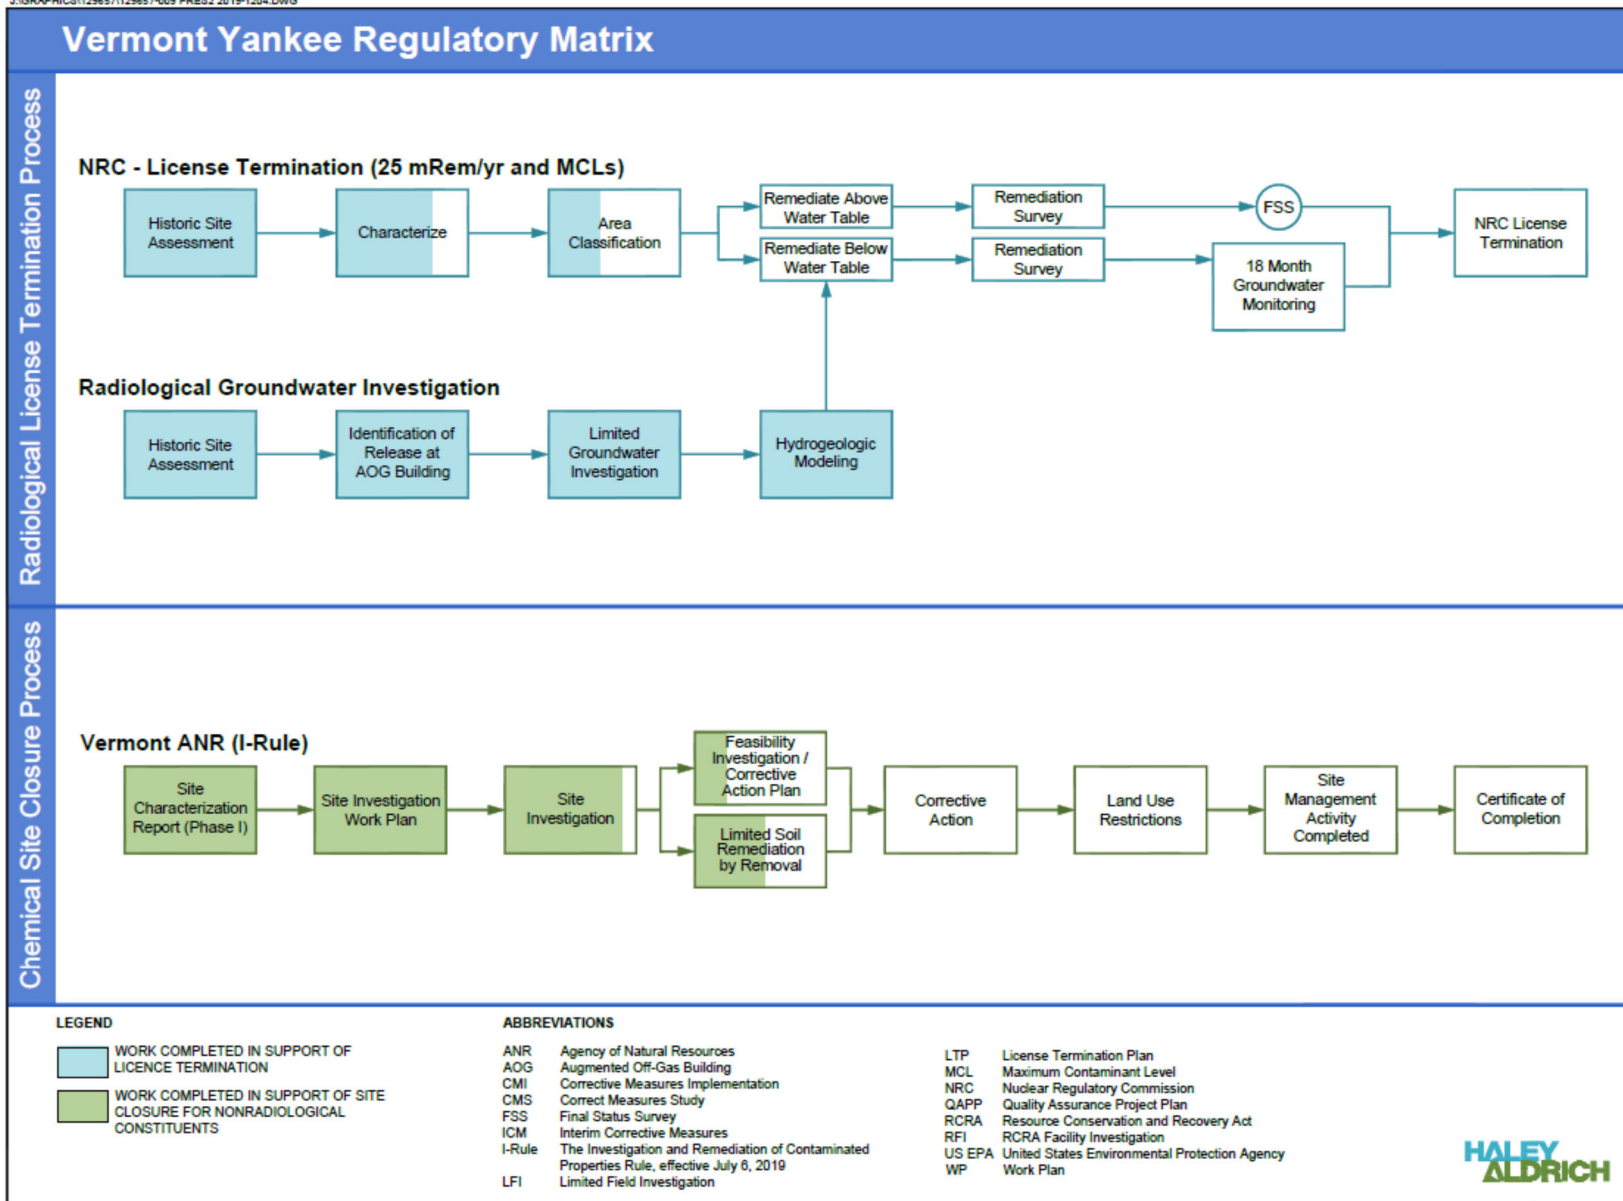

General support to the project in 2019 also included the following characterization activities and tasks;

- NDCAP Support on progress of Characterization and Site Restoration plans
- General Environmental and Permit Support
- Building Characterization Support
 - Building Characterization – Vermont ANR Meeting
 - Building Characterization - Revised Building Characterization WP
 - Building Characterization - Building Characterization Field Sampling
 - Building Characterization - Update Building Materials Sampling Report
 - Building Characterization - Sub-grade Structures WP, Rev A and B
 - Building Characterization - Building Characterization Reports including Sub-grade Structures (per Building), Rev A and B
 - Building Characterization - Building Materials Data Gap WP, Rev A and B
 - Building Characterization Materials - Concrete Management & Disposal Plan
 - Additional Building Characterization Sampling and Vermont ANR Certification
- Various Agency and Subcontractor Coordination
- Environmental and Waste Characterization Support for Non-Radiological aspects
- RCRA Storage Area Closure
- USACE General Permit Application
- Dewatering
 - Permit and Waste Disposal Support
 - Dewatering Support and Dewatering Well Installation, Design and ongoing Support
- Residual Permit and Septic Field Sampling Requirements

Lastly, NorthStar conducted a Baseline Radiological Surface Scan Survey of Lands during 2019 of the facility property with the results producing a high-quality, spatially-robust, and accurately geo-referenced spectral gamma scan data set that is representative of the radiological conditions in surface and near-surface soils at the Vermont Yankee site.

(3) The amount of funds estimated to be required to complete site restoration.

\$23.215 million will be required to complete the site restoration.

CERTIFICATE OF SERVICE


On behalf of NorthStar Vermont Yankee, LLC, I hereby certify that I have this day served NorthStar's report via e-mail to the following entities pursuant to the Docket 8880 Memorandum of Understand Sections 2(h) and 29):

June Tierney Commissioner Vermont Dept. of Public Service June.tierney@vermont.gov	James Porter Director of Public Advocacy Vermont Dept. of Public Service James.porter@vermont.gov Eric.guzman@vermont.gov
Julie Moore Secretary Agency of Natural Resources ANR.notice@vermont.gov Jordan.gonda@vermont.gov	Matt Chapman General Counsel Vermont Agency of Natural Resources Matt.chapman@vermont.gov
The Honorable T.J. Donovan Vermont Attorney General Thomas.Donovan@vermont.gov Justin.kolber@vermont.gov Joshua.diamond@vermont.gov	Mark Levine, MD Commissioner Vermont Department of Health Mark.levine@vermont.gov
David Englander Senior Policy and Legal Advisor Vermont Department of Health David.english@vermont.gov	

DATED at Riverview, Florida, this 31st day of March 2020.

NORTHSTAR VERMONT YANKEE, LLC

By:



Gregory G. DiCarlo
Vice President and General Counsel
