



# Nuclear Decommissioning Citizens Advisory Panel (NDCAP)

May 25, 2017





# Introductions

Joseph R. Lynch  
Sr. Manager, Government Affairs  
Decommissioning – EWC



# Decommissioning Project Status


# VY Decommissioning Update

- Dry Fuel Storage Project
  - ISFSI Pad Construction
    - Construction restarted on March 13th, 2017
    - Rebar placement for the second ISFSI pad is complete
    - Concrete placement is the next project milestone
- Dry Fuel Loading
  - 2017: Approximately 20 Dry Casks
  - 2018: Target loading remainder with 45 total loaded
  - All fuel transferred to the ISFSI: Target 3Q/4Q 2018, pending NRC approvals



# VY Decommissioning Update (Cont'd)

Current ISFSI Pad Configuration

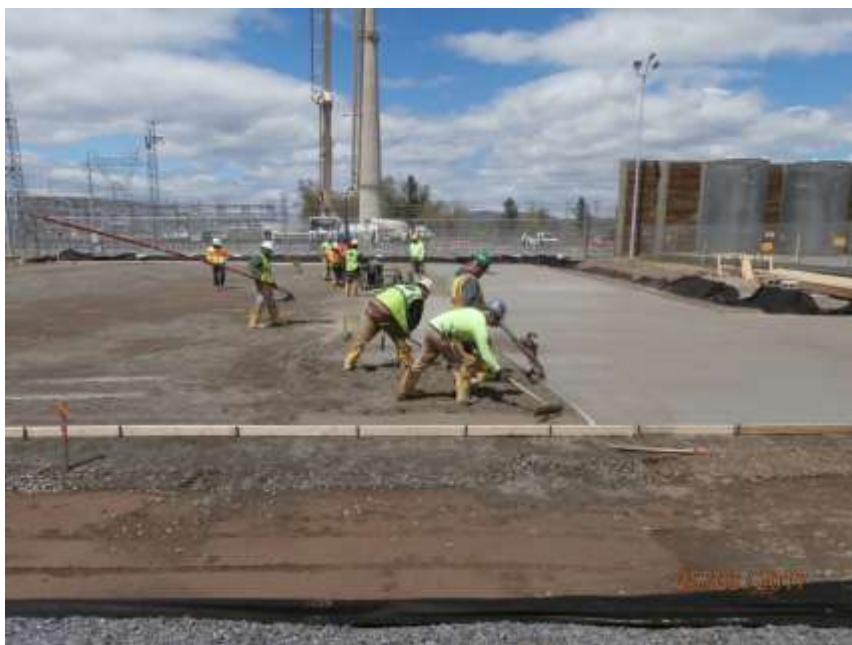

Pouring of Leveling Slab for ISFSI Pad 2



# VY Decommissioning Update (Cont'd)

Rebar Placement for 2<sup>nd</sup> ISFSI Pad



# VY Water Management Update

- Water Management Update

- Intrusion Water Disposition Plan

- Intrusion water retention, shipment and removal plan continues to be implemented.
    - In-leakage prevention projects seeking to further reduce the intrusion of groundwater continue.

- EnergySolutions is providing shipment and disposal services

- Groundwater is being shipped to EnergySolutions licensed disposal site in Tennessee.
    - Shipping approximately three shipments per month at the present intrusion rate to minimize on-site storage.
    - A total of 517,000 gallons have been shipped to date.





# Proposed VY Sale and Accelerated Decommissioning



# Public Service Board Proceeding Update

- First Round of Discovery Requests on Petitioners – March 17th
- Responses to First Round of Discovery Requests – April 26<sup>th</sup>
- DPS filed motion for protective order for confidential documents – May 2<sup>nd</sup>
- NorthStar filed Motion for Special Protocol for Access to Highly Confidential Documents – May 5<sup>th</sup>
- Second Round of Discovery Requests on Petitioners – May 10<sup>th</sup>\*
- NEC filed a Motion for Partial Summary Judgment – May 5<sup>th</sup>
  - Petitioner response to NEC Motion due June 5<sup>th</sup>

\* DPS filed Motion for Extension of Discovery Request Deadline





# Nuclear Decommissioning Trust Update

# Nuclear Decommissioning Trust Update

- The ENVY Nuclear Decommissioning Trust (NDT) balance was \$568.9 Million on March 31, 2017
- The NDT balance was \$570 Million on April 30, 2017
  - The increase was due to positive market performance, partially offset by reimbursements from the NDT. Fund expenses occur periodically throughout the year.
  - Summary of NDT Performance in 2017:
    - \$11.9M in Qualified Withdrawals
    - \$21.7M in Market Gains
    - \$1.4M in Fund Expenses
- The Site Restoration Trust balance was \$23.6 Million on April 30, 2017.
  - Entergy has funded \$20M to date; \$3.6M fund growth.
  - Final \$5M annual contribution to the Site Restoration Trust scheduled for December 2017.



# Open Communication and Transparency

- Nuclear Decommissioning Citizens Advisory Panel (NDCAP)
- Stakeholder Outreach
  - Speaking Engagements
  - Media Interviews
  - Local Advertising
  - Continued Community Involvement
- Tours for Key Stakeholders
- Updated ENVY Decommissioning Website,  
[www.vydecommissioning.com](http://www.vydecommissioning.com)



# Open Communication and Transparency



[History](#) [Get The Facts](#) [News](#) [Document Library](#) [Resources](#) [Contact](#) [Q](#)

WELCOME TO  
**ENERGY VERMONT YANKEE**  
DECOMMISSIONING

## FAQS

View our answers to the most frequently asked questions we receive.

[More Details](#)

## GET THE FACTS

Get accurate information about nuclear power station decommissioning.

[More Details](#)

## DOCUMENT LIBRARY

Visit our Document Library for a full list of State and Federal filings.

[More Details](#)





**QUESTIONS?**

— WE POWER LIFE™

